



# School District No.59 (Peace River South)

---

October 23, 2024

Board of Education

## **RE: Capital Projects Update**

### Crescent Park Elementary School Expansion Project

Since September 20, 2024 the following have occurred:

- October 2, 2024
  - Force Engineering met with Director of Facilities, Manager of Facilities and the Secretary-Treasurer to review complete set of plans. (mechanical, structural and electrical). The engineer will make a rendering of the front of the building and back to share with the school and community.
  
- October 4-11, 2024
  - School District maintenance crew leaders, the Superintendent and the former Director of Facilities reviewed the draft plan and made a list of observations and questions to provide to the engineer for discussion and final design. Some items noted were:
    - Large retaining wall
    - Drainage around the building
  
- October 17, 2024
  - Engineer and Director of Facilities met to review the list of observations and questions above.

The project budget is:


Ministry funding	\$5,000,000
Ministry contingency funding	2,500,000
Board Contribution	<u>1,700,000</u>
Total	\$9,200,000

Spent to date: \$ 78,221

REVISED AREA SUMMARY

ROOM NO.	NAME	AREA (SQM)
150	LIBRARY	104.95
165	CLASSROOM	79.04
165	KINDERGARTEN	80.04
165	KINDERGARTEN	81.13
165	CLASSROOM	79.82
165	CLASSROOM	79.82


TOTAL ADDITION FOOTPRINT 812.45

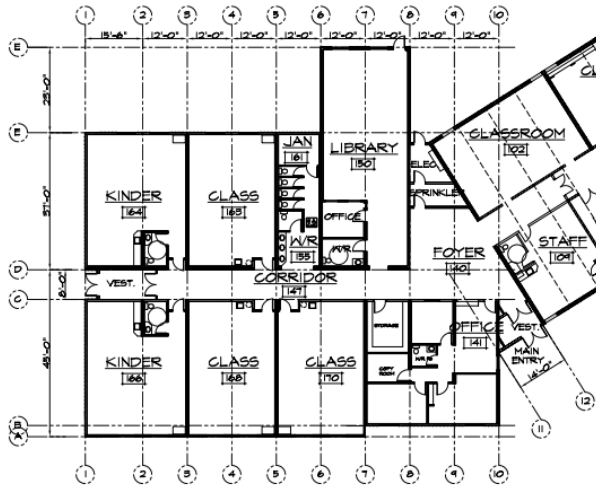

REVISED AREA SUMMARY

ROOM NO.	NAME	AREA (SQM)
150	LIBRARY	104.95
165	CLASSROOM	79.04
165	KINDERGARTEN	80.04
165	KINDERGARTEN	81.13
165	CLASSROOM	79.82
165	CLASSROOM	79.82

TOTAL ADDITION FOOTPRINT 812.45

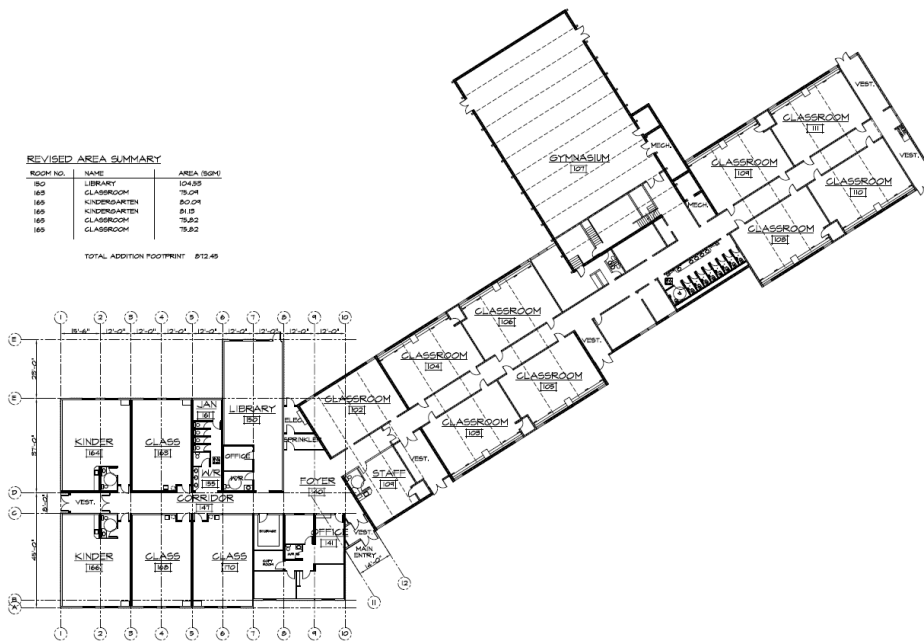

Please follow <https://www.sd59.bc.ca/district/capital-projects> for updates on these projects.

Kim Morris  
Secretary-Treasurer/CFO
