



# School District No.59 (Peace River South)

---

## Crescent Park Elementary School Expansion Project – Update September, 25 2024

- July 2024
  - Meeting with engineer to review finalized drawing and specifications
  - Updated drawings to new Principal for review and comment
  - Updated drawings to the Ministry for approval
  - Ministry review of drawings and comment on classroom size smaller than Ministry design standards
- August 8, 2024 Instructed engineer to redesign to increase the classroom sizes to meet Ministry standards
- September 4, 2024
  - Redesign sent to the Ministry and was approved
  - The redesign will have minimal effect on the budget
  - Ministry gave District approval to move forward with the tendering process for the expansion
- September 11, 2024 Meeting with City to update on the project status.
- September 12, 2024 Engineers and consultants drafting pre-tender package with target of end of September to post on BC Bid.
- September 18, 2024 Presented updated drawings to Crescent Park Staff

The project budget is:

Ministry funding	\$5,000,000
Ministry contingency funding	2,500,000
Board Contribution	<u>1,700,000</u>
Total	\$9,200,000


Spent to date: \$ 78,221

Kim Morris  
Secretary-Treasurer/CFO

**REVISED AREA SUMMARY**

ROOM NO.	NAME	AREA (SQM)
150	LIBRARY	104.55
165	CLASSROOM	75.04
165	KINDERGARTEN	80.04
165	KINDERGARTEN	81.15
165	CLASSROOM	75.82
165	CLASSROOM	75.82

TOTAL ADDITION FOOTPRINT 872.45

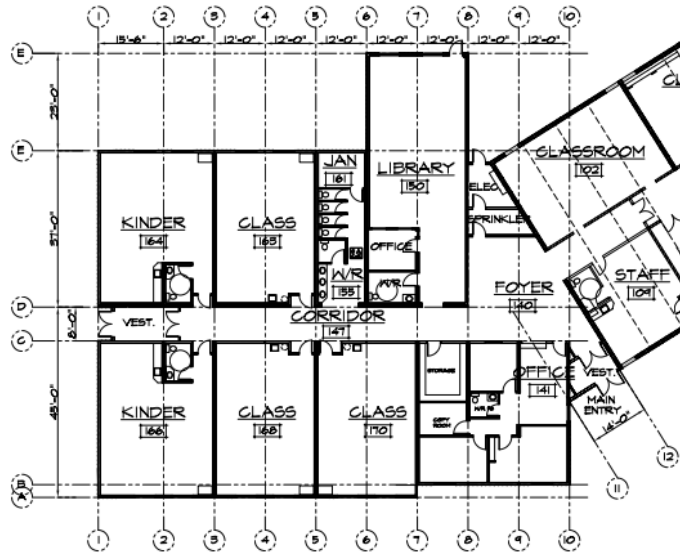

**REVISED AREA SUMMARY**

ROOM NO.	NAME	AREA (SQM)
150	LIBRARY	104.55
165	CLASSROOM	75.04
165	KINDERGARTEN	80.04
165	KINDERGARTEN	81.15
165	CLASSROOM	75.82
165	CLASSROOM	75.82

TOTAL ADDITION FOOTPRINT 872.45

